



WEEKLY CONSTRUCTION UPDATE

| | | |
|--|--------------------------------|-------------------------------------|
| Project Title: Whitman 20-Inch Force Main Replacement CWSRF - 6885 | | Report #: EP - 08-05-2022 |
| Project Location: Brockton, MA and Whitman, MA | From: 8/1/2022 | Week: 16 |
| Client: Whitman, MA | To: 8/5/2022 | Engineer Project #: 279-1901 |
| On-Site Engineer: Bob Fitzgerald, Environmental Partners | Contact: (508) 776-7556 | |
| Contractor: C. Naughton Corp. | | |

CONSTRUCTION ACTIVITIES COMPLETED THIS WEEK:

1. C. Naughton had two crews on site this week; one crew continued the sewer force main installation on Auburn Street and the other installed water services and a hydrant on Auburn Street, and disconnected and reinstalled the water bypass line at the end of Auburn Street. They installed approximately 580 LF of new 20-inch PVC sewer force main along Auburn Street. Approximately 62% of the sewer force main is complete on Auburn Street.
2. C. Naughton detoured traffic onto Beaver Street and Alger Street while the sewer main work was on-going this week. A copy of the detour plan is attached for reference.
3. C. Naughton continued work on Auburn Street on Friday, 8/5. All trenches will be backfilled, compacted, and paved prior to leaving for the weekend.

WEEK LOOK-AHEAD SCHEDULE:

1. C. Naughton will have two crews on site next week (week of 8/8/2022) to continue installation of the new sewer force main and water main on Auburn Street.
2. C. Naughton is maintaining a detour of Auburn Street while water and sewer work is on-going. C. Naughton will maintain access for local residents and for emergency vehicles while the detour is on-going.
3. Daily traffic updates to the Town's project website will be posted to alert residents of anticipated road closures and detours.

PROJECT PHOTOS



Photo 1: Installation of 20-inch PVC Sewer Force Main on Auburn Street



Photo 2: Water Service Connection on Auburn Street at Eliot Woods

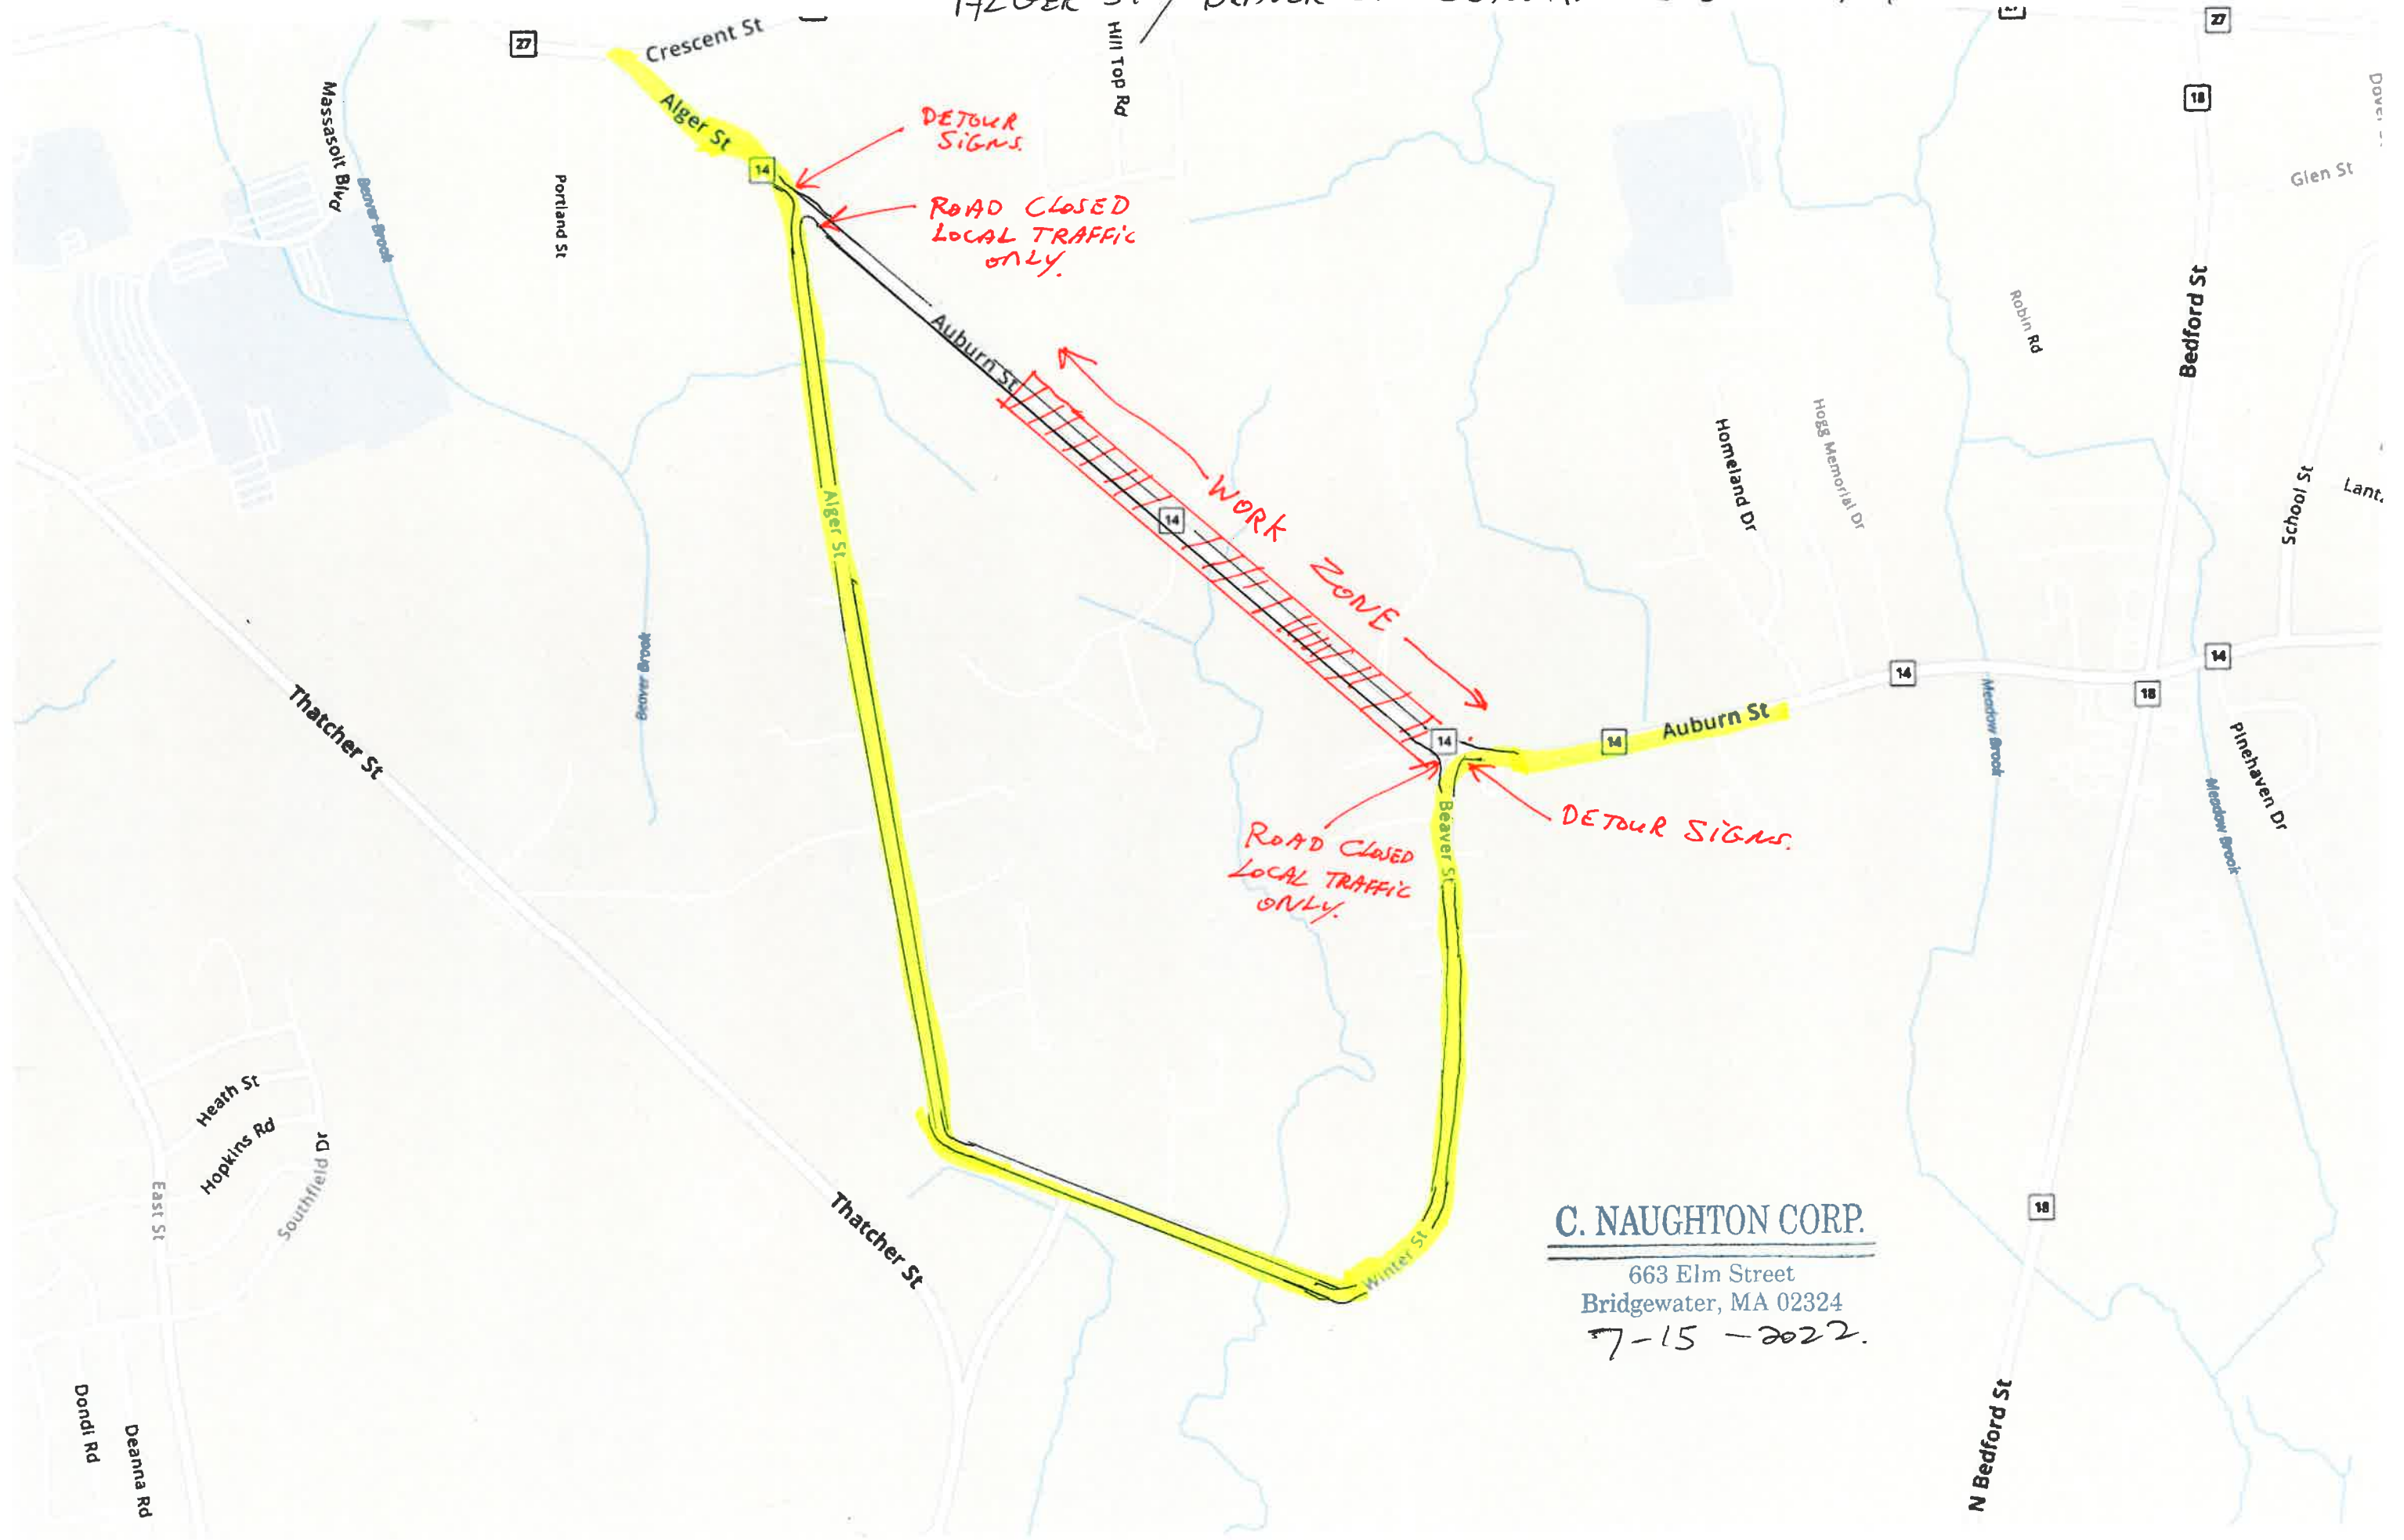


Photo 3: Installation of 20-Inch PVC Sewer Force Main on Auburn Street

Prepared By: Amanda Shanahan, Project Engineer, Environmental Partners Group, LLC

Reviewed By: Andrew Grota, Project Manager, Environmental Partners Group, LLC

ALGER ST / BEAVER ST DETOUR. BEGINS 7-18-2022.



DETOUR SIGNS
ROAD CLOSED LOCAL TRAFFIC ONLY.

WORK ZONE

ROAD CLOSED LOCAL TRAFFIC ONLY.

DETOUR SIGNS.

C. NAUGHTON CORP.
663 Elm Street
Bridgewater, MA 02324
7-15-2022.
