



DAILY WORK & TRAFFIC UPDATE


Project Title: Whitman 20-Inch Force Main Replacement CWSRF - 6885	Date: 8-29-2022
Construction Location: Auburn Street, Whitman, MA	Construction hours: 7 A.M – 5 P.M.

ANTICIPATED WORK SCHEDULE AND TRAFFIC MANAGEMENT:

1. C. Naughton has two crews working today on Auburn Street towards Alger Street. One crew installing the 20" PVC sewer force main by #1235 Auburn Street. The other crew is installing the 12" DI water main on Auburn Street near Meadowview Gardens.
2. C. Naughton will begin the installation of the 20" HDPE sewer force main in the cross-country easement between Auburn Street in Whitman and Alger Street in Brockton on Tuesday, 8/30.
3. Auburn Street will be closed in between Alger Street and Beaver Street for the installation of the 20" sewer force main, other than for local traffic and emergency vehicles. Traffic Management Plans showing the detour routes is attached.
4. Work is expected to take place from 7:00 a.m. until 5:00 p.m. All trenches will be backfilled and paved before leaving for the day.
5. Please note, the emergency access gate located at the rear of the middle school parking lot is closed for public access.

Prepared By: Amanda Shanahan, Project Engineer, Environmental Partners Group, LLC
Reviewed By: Andrew Grota, Project Manager, Environmental Partners Group, LLC

ALGER ST / BEAVER ST DETOUR. BEGINS 7-18-2022.

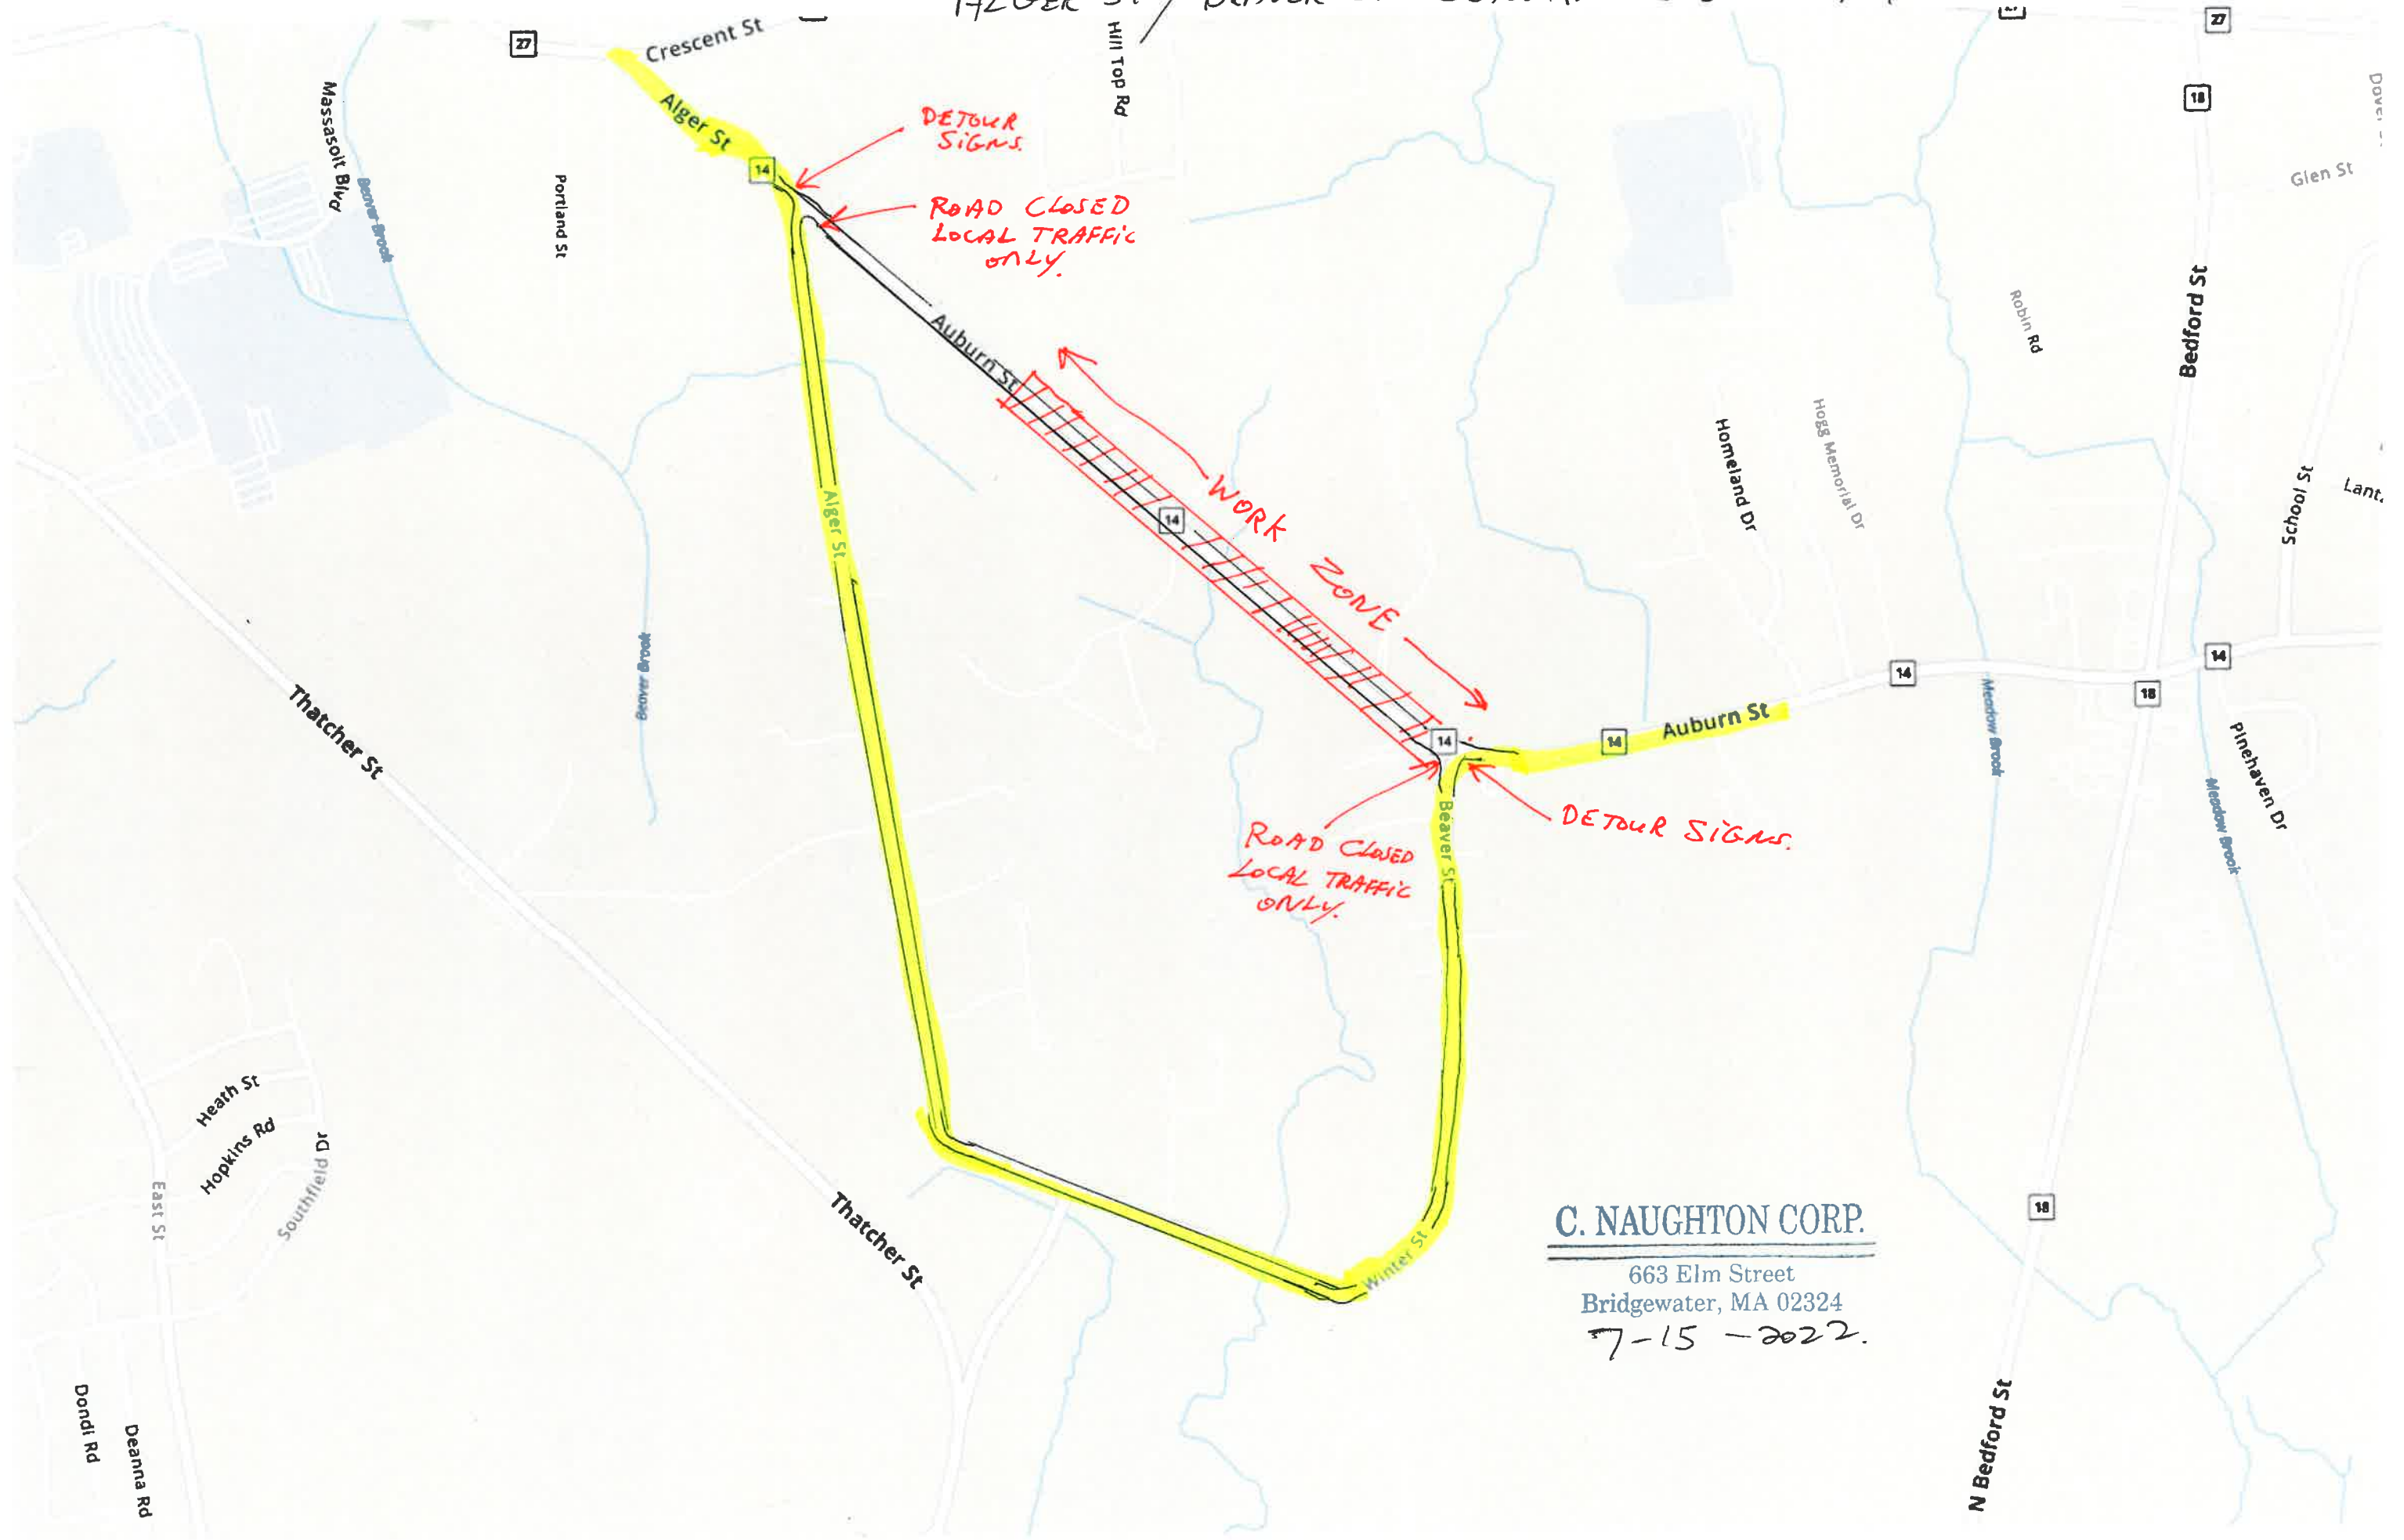

DETOUR SIGNS
ROAD CLOSED LOCAL TRAFFIC ONLY.

WORK ZONE

ROAD CLOSED LOCAL TRAFFIC ONLY.

DETOUR SIGNS.

C. NAUGHTON CORP.
663 Elm Street
Bridgewater, MA 02324
7-15-2022.
